



Report On

2023

CONSTITUENCY PROJECTS IN ZAMFARA STATE

Supported by:



INTRODUCTION

Constituency projects tracking in Zamfara state is one of the activities of the Arewa Research & Development Project (ARDP): as one of the MacArthur Foundation's supported programs of the On Nigeria 2.0 Project. The strategic objectives are focused on reducing corruption through assisting community-based programs and efforts that would strengthen and systemize culture of accountability, transparency and popular participation in the conduct of public affairs. One of the key objectives of this activity is to determine the degree of involvement of the respective communities in the origin of the implementation of the constituency projects and their resourcefulness to societal needs. The activity is also expected to institutionalize or scale up citizens' participation in the incubation process of the constituency projects as well as to galvanize community-based drive in the monitoring and tracking of the projects. The activity is anchored by ZamTracka, which is a collaborative partner in Zamfara state.

ARDP is a research-based non-governmental, non-partisan, non-ethnic and non-religious organization dedicated to the study and examination of major contemporary challenges facing Northern Nigeria and its people, and to provide the needed framework for the strategic thinking and practical program of action needed to address those challenges. Its mission is to nurture the economic and social transformation of the region through undertaking projects that seek to bring together all northern social groups; pooling together the human and material resources in a manner that brings about strategic alliance and synergy with governmental and non-governmental organization working for the progress and well-being of the people in the region.

ZamTracka is a civil society organization based in Gusau, Zamfara state which seeks to champion the cause of civic advocacy with a view to entrenching social accountability in the state. Its main activities have been to source and simplify relevant data on the Zamfara state's fiscal budgets and Zonal intervention projects, and to use same to sensitize the public on the critical public information. The objective is to assist the citizens to follow up on the budgetary capital expenditures and other public projects in their respective communities. This is envisaged to create vanguards of active citizens that demand and ensure effective and efficient service delivery by governments and their agents, as well as stimulate and sustain the demand for open government in Zamfara state

Zonal intervention projects (popularly known as constituency projects) are public projects nominated by federal lawmakers to extend the dividends of democratic government to their various constituencies to spur development at the grassroots level of the country. The projects, by practice are recommended by the executive during the budgeting process. Constitutionally, the national assembly has the oversight obligation on government projects. Given the fact that these projects are nominated by lawmakers, they are morally and even more officially responsible to provide their people with the updates on every project domiciled in their constituency. This is because community member cannot easily access MDAs as they access their elected representatives. Noting that no lawmaker has direct control over the implementation of the projects aside from oversight function, legislators occupy a better position to monitor and proactively ensure the execution of every project by reaching out to the agencies in charge.

In 2023, the total sum of N1.44bn was allocated for constituency projects in Zamfara, the bulk of which are training/empowerment and projects. Capital projects typically involve physical infrastructure development, like building roads or schools, while training/empowerment projects focus on enhancing skills and capacities within a community. In Zamfara State, capital projects contribute to structural improvements, while training/empowerment projects aim to empower individuals and foster sustainable development through skill-building and education. Both play crucial roles in community development, addressing different aspects of growth and well-being. But the crux of the matter in Zamfara State is that the training/empowerment projects are hardly conceived and delivered in the manner to achieve the desired outcomes.

GUSAU/TSAFE FEDERAL CONSTITUENCY

Hon. Kabiru Amadu



01

**Projects
nominated**

01

Executed

0%

**Empowerment
Projects**

00

Unexecuted

100%

Capital Projects

Construction of all-in-one solar streetlights to boost agricultural activities in Gusau/Tsafe Federal Constituency

The project commenced on December 21, 2023, and continued into January 2024. It targeted three different locations: Unguwan Yarima in Gusau, Wanzamai, and the area near General Hospital Tsafe as beneficiaries.

Field assessors identified critical issues with the project's implementation. Although the project title suggests an enhancement of agricultural and related activities within the constituency, the chosen locations do not align with this goal. Notably, Unguwan Yarima, where the lawmaker resides, is an urban area with little agricultural activity. The other locations also fail to support the agricultural focus implied by the project title.

Additionally, the project involved the installation of fifty-two solar streetlights across the sites. Unguwan Yarima received the majority, with thirty installations, while the remaining twenty-two were distributed between the other two locations in Tsafe. A review of the budget reveals a discrepancy between the funds allocated and the actual expenditure, suggesting poor value for money.

In conclusion, the project's outcomes primarily enhance aesthetics and visibility rather than agricultural productivity in the constituency. This discrepancy significantly undermines the project's intended impact. Moreover, it remains unclear whether there is an established system for post-project monitoring or maintenance to address potential issues with the streetlights.



N121m

Executed



BUNGUDU/MARU FEDERAL CONSTITUENCY

Hon. AbdulMalik Zubairu



04

**Projects
nominated**

02

Executed

100%

**Empowerment
Projects**

02

Unexecuted

0%

Capital Projects

Supply of chairs and Desks to some primary schools in Maru/Bungudu Federal Constituency



Maru/Bungudu Federal Constituency

N21m

Executed

The current lawmaker, who replaced the incumbent in the early 2023 general elections, inherited this project from his predecessor. Despite the change in administration, the project was successfully executed.

The initiative introduced a new design of school furniture, where a desktop and seat were integrated into a single unit, rather than using separate chairs and desks. This innovative approach was deployed across ten primary schools within the constituency, with each receiving fifty units.

Field assessors, having visited a few of the beneficiary schools, reported a significant alleviation of the chronic shortage of seating. Previously, children were either crowded into the limited number of available seats or forced to sit on the floor. Now, they have a more comfortable space. This improvement is expected to substantially enhance the standard of the learning environment, thereby improving the quality of both teaching and learning.



Supply of Sewing machines to women in Maru/Bungudu Federal Constituency.



N25m

Executed

This project was specifically designed to support tailors through the umbrella association in both local governments of the constituency. It was executed on January 14, 2024, in Bungudu Local Government, where eighty-four tailors—predominantly women—each received a new sewing machine.

A critical aspect of this project was the thoroughness of the beneficiary selection process, ensuring that the appropriate recipients were chosen. This targeted approach suggests that the beneficiaries are likely to retain and effectively use their new machines to enhance their productivity.

The presence of an organized umbrella association from which the beneficiaries were selected also facilitates efficient post-project monitoring and evaluation. This structure enhances the potential for assessing the project's impact and ensuring continued support and development for the tailoring community.



Agribusiness capacity building and starter-pack for women and youth in Maru/Bungudu Federal Constituency



N50m

Unexecuted

Field assessors conducted a thorough review across the constituency to verify the execution of this project. However, all the feedback collected was negative. Constituents consistently reported that there was no evidence to suggest the project had been implemented, indicating a significant discrepancy between planned activities and actual outcomes.

Supply of grains in Maru/Bungudu Federal Constituency



Maru/Bungudu Federal Constituency

N25m

Unexecuted

Field assessors conducted a thorough review across the constituency to verify the execution of this project. However, all the feedback collected was negative. Constituents consistently reported that there was no evidence to suggest the project had been implemented, indicating a significant discrepancy between planned activities and actual outcomes.

BAKURA/MARADUN FEDERAL CONSTITUENCY

Hon. Muhammad Ahmed



03

**Projects
Nominated**

02

Executed

75%

**Empowerment
Projects**

01

Unexecuted

25%

Capital Projects

Training for rural women on modern renewable energy device for food processing and preservation in Bakura/Maradun Federal Constituency



Bakura/Maradun
Federal Constituency

N40m

Executed !

The lawmaker, having unseated the incumbent in the early 2023 general elections, inherited this project from his predecessor. Although the project was executed, it was not without significant flaws. It took place on March 19th at the College of Agricultural Sciences in Bakura Local Government. Fifty beneficiaries were trained, each receiving a token of N20,000 and a certificate of participation.

Notably, there was a clear mismatch between the project as planned and as executed. The training exclusively involved male participants, with no women included, and focused solely on basic solar technology rather than using renewable energy for food processing and preservation as originally intended. Furthermore, the training lasted only one day, contrary to the six days advertised on the project banner. These discrepancies suggest that the initially nominated project was abandoned in favor of a different, less comprehensive initiative.

Given the deviation from the proposed plan and the lackluster execution, the project can be considered to have provided poor value for money. This undermines the potential for effective evaluation and impact assessment, rendering any such efforts likely futile.



Supply and installation of solar streetlights in Bakura/Maradun Federal Constituency.



Bakura/Maradun
Federal Constituency

N51m

Executed

The project to install streetlights commenced on December 21, 2023. As of the time this report was prepared, the exact number of streetlights installed could not be reconciled. Nonetheless, field assessors managed to evaluate some locations that benefited from the project to conduct needs assessments and determine the project's relevance to local challenges.

The feedback from these assessments was largely positive. Most locations surveyed had significant visibility issues at night, and the additional lighting provided by the streetlights has been beneficial. This improvement is particularly important given the deteriorating security situation, as it helps illuminate areas and enhance the liveliness of the surroundings. Notable locations that received lighting include mosques, Islamic schools, open markets, and rural areas deep within the community.

However, it remains unclear if there is a post-project monitoring and maintenance system in place to ensure ongoing maintenance and repairs of the streetlights. This lack of information raises concerns about the long-term sustainability and effectiveness of the project.



Construction of 2 solarpowered boreholes in Bakura/Maradun Federal Constituency.



Bakura/Maradun
Federal Constituency

N30m

Unexecuted

Field assessors conducted a thorough review across the constituency to verify the execution of this project. However, all the feedback collected was negative. Constituents consistently reported that there was no evidence to suggest the project had been implemented, indicating a significant discrepancy between planned activities and actual outcomes.

ZAMFARA WEST SENATORIAL DISTRICT

Sen. AbdulAziz Yari



01

**Projects
Nominated**

01

Executed

0%

**Empowerment
Projects**

00

Unexecuted

100%

Capital Projects

Supply and installation of solar streetlights to enhance agric outputs in Zamfara West Senatorial District



Zamfara West
Senatorial District

N214m

Executed

The lawmaker, having won the senate seat in the early 2023 general elections, inherited this project from his predecessor. The project's implementation spanned from December 2023 through January 2024. At the time of reporting, the exact number of streetlights installed could not be verified.

Field assessors conducted a needs assessment in several areas that reportedly benefited from this project, including Titin 'yar Yelwa, Titin 'Yar Hudu, 'Yan Kifi, Karfi Area, 'Yar Zamau, and Titin Stadium, all within the senatorial zone. The objective was to determine if the intervention was enhancing agricultural outcomes as stated in the project's title. However, the outcome was largely negative. Most of the locations were semi-urban, making it difficult to associate them with any significant agro-allied activities. Therefore, it appears that the project primarily enhances aesthetics and nighttime visibility rather than boosting agricultural outcomes in the zone.

Additionally, it remains uncertain whether there is a post-project monitoring and maintenance system in place to address routine maintenance and repairs of the streetlights, which raises concerns about the project's sustainability and long-term effectiveness.



GUMMI/BUKKUYUM FEDERAL CONSTITUENCY

Hon. Sulaiman Abubakar



03

**Projects
Nominated**

02

Executed

75%

**Empowerment
Projects**

01

Unexecuted

25%

Capital Projects

Completion of primary healthcare center at Gamji in Gummi/Bukkuyum Federal Constituency

This project, a 31-bed primary healthcare center located in the Gamji area of Illela ward within Gummi Local Government, was initiated in November 2020 but was abandoned for over three years until recently. This intervention therefore aimed to complete the construction and prepare the facility for public use.

Field assessors monitoring the project reported that all structural work had been finished, with only the painting of the building remaining. However, it is currently unclear when the facility will be fully furnished and opened to the public.

Given the demographics of the ward and its surroundings, once operational, this healthcare center will be the only major active medical facility in the region, catering to patients from far-reaching areas. The potential impact of this facility on local healthcare accessibility is therefore significant.

Nonetheless, similar interventions often fail to reach their full potential due to a lack of robust involvement of the community and other critical stakeholders in managing and maintaining the facilities. It is hoped that this project will be an exception, with the community taking ownership and ensuring the sustainability of the healthcare center.



Gummi/Bukkuyun
Federal Constituency

N31m

Executed



Supply of 18 seater Bus in Gummi/ Bukkuyum Federal Constituency



Gummi/Bukkuyun
Federal Constituency

N50m

Executed !

The supply of an 18-seater bus was officially announced on March 16, 2024, at a ceremony held at the lawmaker's constituency office in Gummi Local Government. During this event, at least 10 other vehicles were also declared, though these were distributed among some of the lawmaker's designated loyalists.

The 18-seater bus, which bore a sticker indicating its use as a utility vehicle for student affairs within the constituency, raised several questions. The necessity of this procurement, the future custodian of the vehicle, its intended usage scope, and responsibilities for its upkeep remain unclear. These concerns stem from previous experiences with similar projects, where vehicles intended for public benefit ended up being used personally by the lawmaker, not serving the intended community purpose. Another pattern was noted particularly last year when a vehicle procurement project nominated by the lawmaker was never executed.

Furthermore, the budget allocation for this project was N50 million, which appears excessive given the vehicle's condition. A thorough assessment revealed that the market value of a brand-new Toyota 18-seater bus ranges between N27 million and N29 million, yet the bus provided was a used one. This discrepancy highlights a significant lack of value for the money spent on the project.



Development of value chain addition and large ruminants through processing for market access and economic empowerment in Gummi/Bukkuyum Federal Constituency



Gummi/Bukkuyum
Federal Constituency

N40m

Unexecuted

Field assessors conducted a thorough review across the constituency to verify the execution of this project. However, all the feedback collected was negative. Constituents consistently reported that there was no evidence to suggest the project had been implemented, indicating a significant discrepancy between planned activities and actual outcomes.

KAURA/BIRNIN MAGAJI FEDERAL CONSTITUENCY

Hon. Aminu Sani Jaji



02

**Projects
Nominated**

02
Executed

100%
**Empowerment
Projects**

00
Unexecuted

0%
Capital Projects

Skill acquisition for youth and women in Kaura/Birnin Magaji Federal Constituency

N25m

Executed !

The lawmaker, who took office following the early 2023 general elections, inherited and carried out this project over two days, from July 17th to 19th, 2023, at the Federal Polytechnic in Kaura Namoda. The project involved training one hundred beneficiaries from the twenty-one wards of the constituency in cosmetology, specifically in making liquid soap and Vaseline. Each participant received a certificate of attendance and a token of N15,000 as startup capital to initiate a small-scale business.

However, based on observed trends from similar projects, it is challenging to determine the actual impact. Often, the intended beneficiaries—the ones who could genuinely benefit from such training—are not the ones who end up being trained. Additionally, the lack of post-project monitoring and evaluation makes it difficult to assess the project's effects on both the individual participants and the constituency at large. Consequently, many trainees tend to become inactive post-project, as the startup capital provided is frequently used for immediate personal needs rather than for applying the learned skills.

Therefore, it is crucial that such interventions focus on selecting the appropriate pool of trainees and include a robust plan for post-project evaluation. This approach will help ensure that the projects achieve lasting impact and sustainability, aligning with their intended goals.



Supply of agricultural inputs in Kaura/Birnin Magaji Federal Constituency.

N50m

Executed 

The lawmaker, who won the seat in the early 2023 general elections, inherited this project from his predecessor and proceeded with its implementation on July 17, 2023, at the Federal Polytechnic, Kaura Namoda. Notably, this project commenced on the same day as another similar initiative.

While the exact number of beneficiaries remains unclear, it is reported that they were real-time farmers representing each of the twenty-one wards of the constituency. Given the constituency's predominantly agrarian character, interventions aimed at enhancing agricultural productivity are crucial. However, the support provided through this project—offering each beneficiary just one sack of fertilizer—may be substantially inadequate to meet the needs of the farmers and could fall short of significantly boosting agricultural output in the region. This raises concerns about the sufficiency and effectiveness of the assistance provided.



SHINKAFI/ZURMI FEDERAL CONSTITUENCY

Hon. Bello Hassan



03

**Projects
Nominated**

03

Executed

75%

**Empowerment
Projects**

00

Unexecuted

25%

Capital Projects

Renovation and construction of drainage in Shinkafi town in Shinkafi/Zurmi Federal Constituency

N100m Executed

The project targeting erosion-prone and waterlogged communities within several wards of Shinkafi Local Government began on November 12, 2023. Field assessors visited some of these wards to evaluate the construction quality and assess its impact on the communities. The construction work, utilizing steel-reinforced concrete techniques, was found to be satisfactory overall. However, concerns were raised regarding the drainage systems being somewhat shallow, which might lead to overflowing during heavy rainfall.

Additionally, the uncovered nature of these drainage systems poses a risk of becoming breeding grounds for mosquitoes, potentially increasing malaria transmission unless they are properly drained and maintained. Except for one location in Katuru ward where the project has not been fully completed, all other targeted areas have seen the completion of their projects.

Overall, the intervention has made a tangible impact on the constituency. In an era of climate change with unpredictable rainfall patterns, such infrastructure improvements are crucial for addressing the environmental challenges faced by the community, enhancing their resilience against natural elements.



Supply of gas cylinders in Shinkafi/ Zurmi Federal Constituency

N21m

Executed

This project, conducted on June 17, 2023, was a comprehensive empowerment initiative aimed at supporting petty traders in the constituency, distinct from merely supplying gas cylinders. A total of 180 beneficiaries were selected from the twenty-one wards of the constituency: Shinkafi North, Shinkafi South, and Zurmi ward each contributed twelve beneficiaries, while the other eighteen wards provided eight each. These individuals included tea and bread sellers, beans cake sellers, and soya beans cake sellers.

On the day of execution, various items were distributed to aid these small scale traders in their businesses. The items included cartons of Indomie quick noodles, gallons of groundnut oil, sacks of beans, large frying pans, and 3kg gas cylinders. This method of empowerment, providing tangible business resources rather than cash, was designed to ensure immediate utility and prevent the funds from being diverted to non-business uses. It aimed to foster sustainable growth and immediate improvement in the beneficiaries' trading capacities.

Despite the project's potential for significant impact, it remains unclear whether there is a post-project monitoring and evaluation framework in place to directly assess the impact and challenges faced by the beneficiaries. This oversight could affect the long-term sustainability and effectiveness of the empowerment initiative.



Educational empowerment to the students of Shinkafi/Zurmi Federal Constituency

N50m

Executed



This project was initiated in response to the national increase in tuition fees for public universities, addressing the educational support needs within one of the state's least educated and developed constituencies. Its primary goal is to assist those who have managed to pursue tertiary education—a critical concern given the constituency's background.

However, the implementation framework for this project remains unclear. Field assessors were unable to determine the amount each student-beneficiary received, making it difficult to assess whether the financial support was distributed evenly across all recipients. Furthermore, the criteria used for selecting beneficiaries and the total number of students supported by the scheme were not transparent.

Assessors did obtain a list of beneficiaries from Usmanu Danfodio University in Sokoto, which included detailed information about the students. Yet, it remains uncertain whether other universities or institutions are included in this support scheme. This lack of clarity complicates efforts to fully evaluate the project's reach and effectiveness.




STUDENTS LIST	
1	...
2	...
3	...
4	...
5	...
6	...
7	...
8	...
9	...
10	...



STUDENTS LIST	
1	...
2	...
3	...
4	...
5	...
6	...
7	...
8	...
9	...
10	...



STUDENTS LIST	
1	...
2	...
3	...
4	...
5	...
6	...
7	...
8	...
9	...
10	...



STUDENTS LIST	
1	...
2	...
3	...
4	...
5	...
6	...
7	...
8	...
9	...
10	...

ZAMFARA NORTH SENATORIAL ZONE

Sen. Sahabi Ya'u



02

**Projects
Nominated**

00

Executed

100%

**Empowerment
Projects**

02

Unexecuted

0%

Capital Projects

Empowerment for women and youths of Zamfara North Senatorial District.



Zamfara North
Senatorial District

N100m

Unexecuted

Field assessors conducted a thorough review across the constituency to verify the execution of this project. However, all the feedback collected was negative. Constituents consistently reported that there was no evidence to suggest the project had been implemented, indicating a significant discrepancy between planned activities and actual outcomes.

Agro-business supplies for small scale farmers in Zamfara North Senatorial District



Zamfara North
Senatorial District

N100m

Unexecuted

Field assessors conducted a thorough review across the constituency to verify the execution of this project. However, all the feedback collected was negative. Constituents consistently reported that there was no evidence to suggest the project had been implemented, indicating a significant discrepancy between planned activities and actual outcomes.

ZAMFARA CENTRAL SENATORIAL ZONE

Sen. Ikira Aliyu Bilbis



01

**Projects
Nominated**

00
Executed

100%
**Empowerment
Projects**

01
Unexecuted

0%
Capital Projects

NHIS vital health contribution to social health insurance scheme in Zamfara Central Senatorial District



Zamfara Central
Senatorial District

N214m

Unexecuted

Field assessors conducted a thorough review across the constituency to verify the execution of this project. However, all the feedback collected was negative. Constituents consistently reported that there was no evidence to suggest the project had been implemented, indicating a significant discrepancy between planned activities and actual outcomes.

ANKA/MAFARA FEDERAL CONSTITUENCY

Hon. Muhd Isa Anka



03

**Projects
Nominated**

02

Executed

75%

**Empowerment
Projects**

01

Unexecuted

25%

Capital Projects

Training for rural women on modern renewable energy devise for food processing and preservation in Anka/Mafara Federal Constituency

N41m

Executed

The lawmaker, who assumed office after his victory in the early 2023 General Elections, implemented this project on March 9, 2024, at the Karma Hotel in Gusau. Due to the volatile security situation in the constituency and surrounding areas, 50 women were transported to the state capital for the training. The session focused on educating participants about renewable energy and its applications in food processing and preservation.

At the conclusion of the training, each beneficiary received a pellet fueled stove and a token of N20,000. However, the criteria for selecting participants were unclear, and field assessors noted that many of the women did not appear to be engaged in trades that would benefit from this intervention. This raises questions about the impact and target efficacy of the project.

Financially, the total start-up capital distributed amounted to N1 million. While the cost of the stoves distributed was not specifically determined, the overall basic execution of the project did not seem to justify the total budget allocated. Therefore, this project fails to meet the value for money criterion, casting doubts on its financial management and effectiveness.



Provision of skill acquisition equipments in Anka/Mafara Federal Constituency

N30m

Executed

The project, executed on March 9, 2024, at the Karma Hotel in Gusau, involved transporting 50 beneficiaries from the volatile constituency to the state capital for safety reasons. The training session focused on renewable energy, specifically teaching participants how to harness solar energy for both domestic and commercial purposes, and included practical guidance on setting up solar energy systems. This foundational knowledge was intended to spur the beneficiaries toward entrepreneurship.

Each participant received a token of N20,000 at the end of the daylong session to help start their ventures. However, field assessors were unable to determine the criteria used for selecting beneficiaries or whether there was any post-project monitoring and evaluation plan in place to gauge the project's effectiveness.

Financially, the total start-up capital given to the beneficiaries amounted to N1 million only. Considering the overall execution of the project, this expenditure appears disproportionate, leading to concerns about the project's value for money. The basic implementation does not seem to justify the total funds allocated, indicating that the project may not meet the expected standards of financial efficiency and impact.



Supply and installation of integrated solar streetlights in Anka/Mafara Federal Constituency.



Anka/Mafara
Federal Constituency

N50m

Unexecuted

Field assessors conducted a thorough review across the constituency to verify the execution of this project. However, all the feedback collected was negative. Constituents consistently reported that there was no evidence to suggest the project had been implemented, indicating a significant discrepancy between planned activities and actual outcomes.

METHODOLOGY

This looks at whether Citizens' Engagement avenues such as town hall meeting were used to engage citizens in the nomination process.

This reviews the level of execution of all project Nominated by the respective law-makers.

Index C Looks at the project nomination and draws distinction between capital project and not so impactful Empowerment/Project



Any Civic engagement strategy utilized takes 1 point. its absence is an automatic 0.



$$\frac{\text{Executed Projects}}{\text{Total Number of Projects}}$$



$$\frac{\text{Capital Projects Nominated}}{\text{Total Number of Projects}}$$

Lawmaker Performance on **Index A**

Index A looks whether Citizens' Engagement avenues such as town hall meeting were used to engage citizens in the nomination and execution process.

Lawmaker	Index A Rating
Sen. Ikira Aliyu Bilbis	0
Sen. Sahabi Ya'u	0
Sen. AbdulAziz Yari	0
Hon. Kabiru Amadu	0
Hon. Abdulamalik Zubairu	0
Hon. Aminu Sani Jaji	0
Hon. Muhammad Ahmad	0
Hon. Muhammad Isa	0
Hon. Sulaiman Abubakar Gummi	0
Hon. Bello Hassan Shinkafi	0

Lawmaker Performance on **Index B**

Index B assesses level of project completion. Lawmakers that rank higher on this index have a higher project completion rate.

Lawmaker	Index B Rating
Hon. Kabiru Amadu	1
Sen. AbdulAziz Yari	1
Hon. Aminu Sani Jaji	1
Hon. Bello Hassan	1
Hon. Sulaiman Gummi	0.66
Hon. Muhd Isa Anka	0.66
Hon. Muhammad Ahmad	0.66
Hon. AbdulMalik Zubairu	0.50
Sen. Ikira Aliyu	0
Sen. Sahabi Ya'u	0

Lawmaker Performance on **Index C**


Representatives with a higher ranking on Index C have prioritized capital projects in their nominations. While in contrast, those with lower ranking nominated projects that are not legacy based and whose real impact cannot be fully determined

Lawmaker	Index C Rating
Hon. Kabiru Amadu	1
Sen. AbdulAziz Yari	1
Hon. Muhammad Ahmad	0.66
Hon. Bello Hassan	0.33
Hon. Sulaiman Gummi	0.33
Hon. Muhd Isa Anka	0.33
Hon. Aminu Sani Jaji	0
Hon. AbdulMalik Zubairu	0
Sen. Ikira Aliyu	0
Sen. Sahabi Ya'u	0

2023 Zamfara Federal Lawmakers' Constituency Projects Performance index

Ranking	Lawmaker	Constituency	Commulative Index Score
1st	Sen. AbdulAziz Yari	Zamfara West Zone	2
1st	Hon. Kabiru Amadu	Gusau/Tsafe	2
3rd	Hon. Bello Hassan	Shinkafi/Zurmi	1.33
4th	Hon. Muhammad Ahmad	Bakura/Maradun	1.32
5th	Hon. Amin Sani Jaji	Kaura/Birnin Magaji	1
6th	Hon. Sulaiman Abubakar	Gummi/Bukkuyum	0.99
6th	Hon. Muhammad Isa Anka	Anka/Mafara	0.99
8th	Hon. AbdulMalik Zubairu	Bungudu/Maru	0.50
9th	Sen. Sahabi Ya'u	Zamfara North	0
9th	Sen. Ikira Aliyu	Zamfara Central	0

SUMMARY OF THE TRACKING EXERCISE

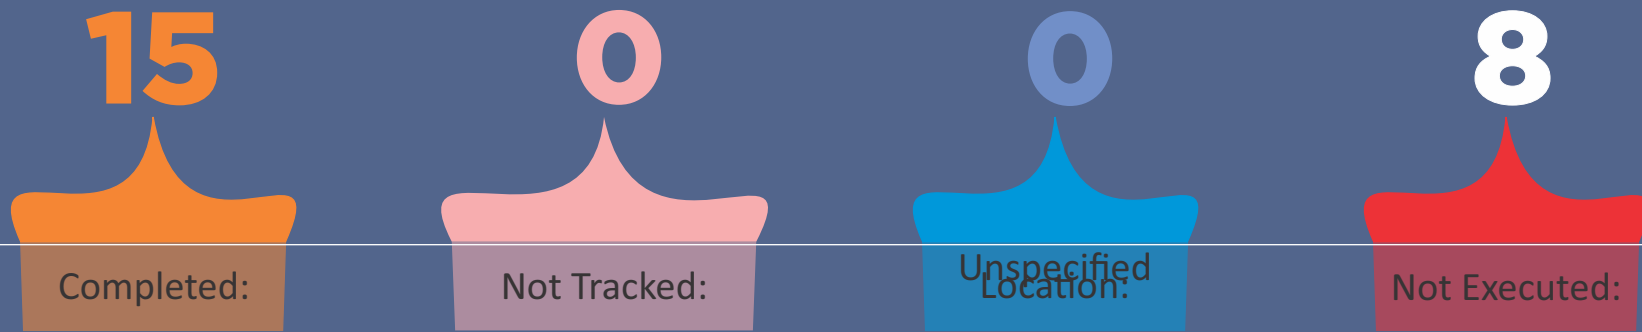

23

**TOTAL NUMBER
OF PROJECTS**

STATISTICAL BREAKDOWN



Total Amount Allotted

N1.44bn


29

Training/Empowerment
Projects

06

Capital Projects

PERCENTAGE OF PROJECTS' COMPLETION

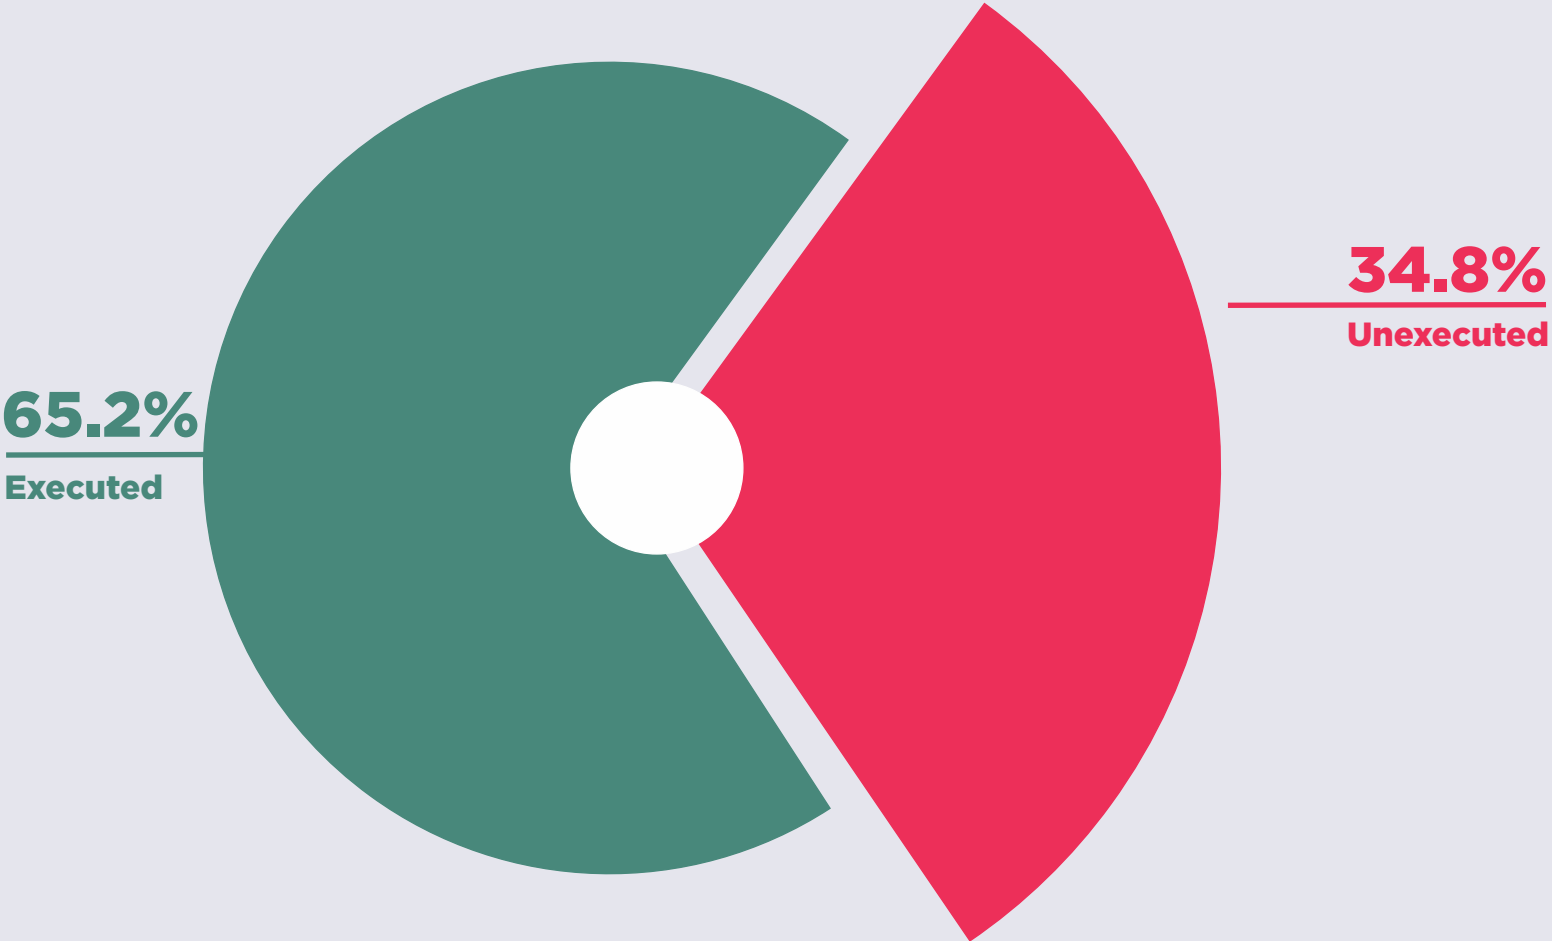



Follow up and track implementation of public projects within your vicinity



Upload pictures, add comments, send feedback to institutions



Announce and share with your friends, family and thousand across the state



Continue to engage.

No. 40, Sadiqu Sadiq Road,
Tudun Wada, Gusau, Zamfara State.

 [f/t](#) @ZamTracka

 ZamTracka@gmail.com

#AskQuestions
